


Capital Markets Day 2 September 2009

Aitik Expansion Project – Status and Site Visit Peter Richardson General Manager Aitik



2009-08-31

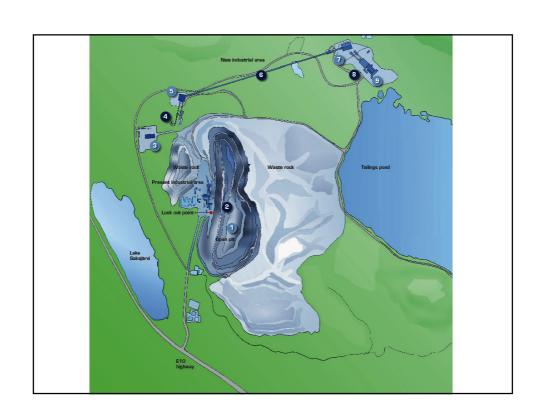

Project status, August 2009

- Procurement started in December 2006
- Tunnel construction started in May 2007
- Some early works started in October 2007
 - Excavating, earth moving and road construction
- Civil work started after the environmental permit, January 25, 2008
- · Tunneling is finished
- Most of the civil work is finished
- Installation of process equipment and media is ongoing
- · Project is on plan





Roliden A

3






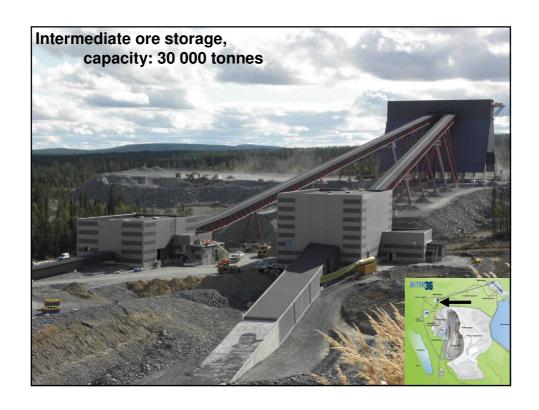

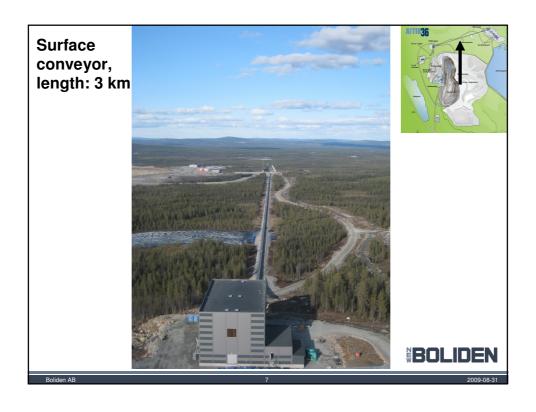



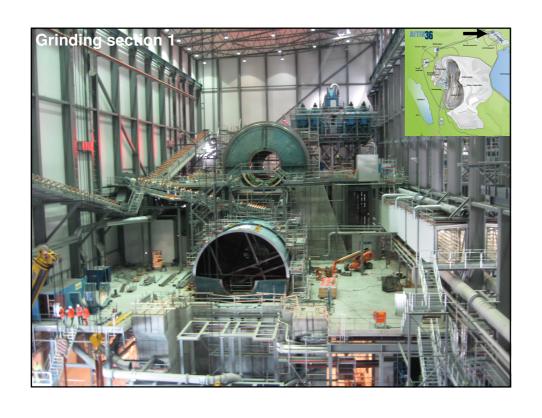



AITIK – Commissioning

Time plan

w. 0932 Signal test, control system

w. 0941 Start cold test crushers and conveyors

• w. 0949 Start cold test mills

w. 0950 Start hot tests

w. 1002 Start hand over tests


100401 Production mill section 1

• 100701 Production mill section 2



oliden AR

11

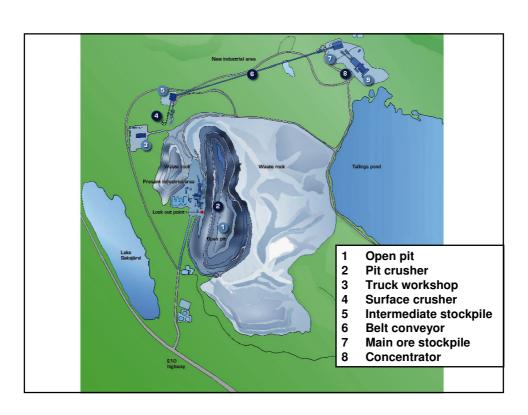

AITIK – Safety instructions

- · Personal protective equipment:
 - Helmet with chinstrap, protective shoes, high-visibility clothing
- · Keep to the group
- · Watch out for heavy transports
- · Watch out for uneven surfaces
- · Respect roped-off areas
- Don't walk under loads on cranes

REMEMBER - THIS IS A CONSTRUCTION SITE!



oliden AB 13 2
